



JACKSON ROAD (CR 534) ROADWAY IMPROVEMENTS

ERI Job #:30750 83

Borough of Berlin & Township of Berlin

County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #1

July 29, 2024 to August 9, 2024



Figure: 1 – Installation of Type B Inlet and 12” RCP at the intersection with Washington Street

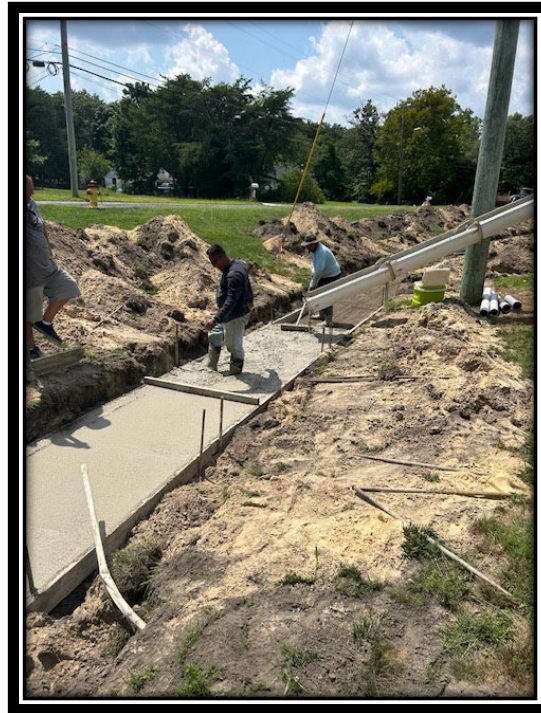


Figure: 2 – Installation of 6" thick, reinforced concrete drainage swale along the frontage of 117 Jackson Road



Figure: 3 – HMA trench restoration over newly installed 12" RCP at the intersection with Washington Street

Work Completed the Weeks of July 29, 2024 and August 5, 2024:

Arawak's pipe subcontractor, CTX, mobilized to the site on Monday, July 29, 2024. CTX's pipe crew began installation of drainage improvements along both the southbound and northbound lanes between Washington Street and Hamilton Street. The pipe crew installed 218 linear feet of 12" RCP, 2 B inlets, 1 E inlet, 1 concrete headwall, reconstructed 3 inlets, 168.9 square yards of concrete drainage swale, set 3 B inlet casting and dug 8 cubic yards of test pits. Arawak's tree subcontractor also mobilized to the site and removed 6 trees and cleared 43 square yards of brush.

- #2: Portable Message Boards – 2 Units**
- #4: Traffic Director, Flagman – 166 MH**
- #39: Tree Removal, 6" to 18" Diameter – 3 Units**
- #40: Tree Removal, 18" to 30" Diameter – 3 Units**
- #59: Excavation, Test Pit – 8 CY**
- #63: 12" RCP – 218 LF**
- #68: Set Inlet Type B Casting – 3 Units**
- #71: Reconstruct Stormwater Structure Using New Casting – 3 Units**
- #72: Inlet, Type 'B' – 2 Units**
- #74: Inlet, Type 'E' – 1 Unit**
- #75: Concrete Headwall – 1 Unit**
- #76: Concrete Drainage Swale, Reinforced, 6" Thick – 168.9 SY**

Anticipated Work for the Weeks of August 12, 2024 & August 19, 2024

CTX's pipe crew will complete the installation of the proposed storm sewer improvements and their concrete subcontractor, Batata, will mobilize to the site to begin concrete improvements.

- Bid Opening Date: January 9, 2024**
- Notice to Proceed Date: June 10, 2024**
- Start Date: June 11, 2024**
- Anticipated Completion Date: October 8, 2024**
- Contract Completion Date: November 7, 2024**
- Contract Completion Percentage: 12.24%**
- Initial Project Cost: \$1,593,000.00**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
