

Department of Public Works

Almar Dyer  
Commissioner Liaison

Robert Harris  
Director



Making It Better, Together.

Department of Public Works  
Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
phone 856.566.2980  
fax 856.566.2988  
highway@camdencounty.com  
CamdenCounty.com

**Kaighn Avenue Dam – East Tide Gate  
(NJDEP Dam #31-066)  
*Bid No. B1-24***

*Township of Pennsauken and City of Camden  
Camden County, New Jersey*

**CED Project No. 230005437G2**

***Progress Report #2***  
*Monday, May 13, 2024 to Friday, May 24, 2024*



*Figure:1*  
*Driscoll Construction continues to close cofferdam.*


Department of Public Works

Almar Dyer  
Commissioner Liaison

Robert Harris  
Director



Department of Public Works  
Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
phone 856.566.2980  
fax 856.566.2988  
highway@camdencounty.com  
CamdenCounty.com

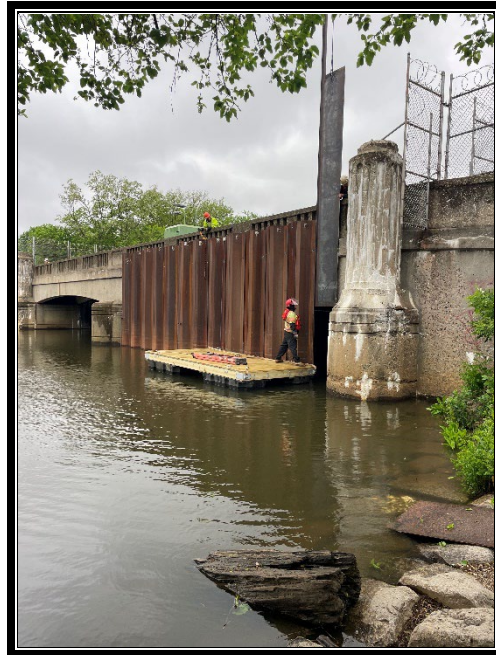

*Figure 2: Driscoll Construction completing cofferdam work.*



*Figure 3: Driscoll Construction selected staging area on east side of North Park Drive.*

- **Work Completed this week:**
  - Contractor completed cofferdam work.
  - Continued dewatering operation.
  - On site meeting to select staging area east of North Park Drive.
  - Contractor began to mobilize staging area.
  
- **Items completed this period:**
  - Item No. 4 – General Work
  - Item No. 6 - Protection of Work
  - Item No. 8 - Cofferdam Work / Dewatering
  - Item No. 9 – Existing Walkway & Hydraulic Lifting System Removal
  
- **Progress Next Two Weeks:**
  - Continue cofferdam and dewatering.
  - Remove tide gate and begin repairs.
  
- **Next Progress Meeting:**
  - The next Progress Meeting has been rescheduled for Thursday, May 30, 2024 at 2:30 PM.
    - Bid Award Date: March 21, 2024
    - Notice to Proceed: April 29, 2024
    - Start Date: May 7, 2024
    - Substantial Completion Date: October 25, 2024
    - Stop Work: N/A
    - Amended NTP: N/A
    - Final Completion Date: November 14, 2024
    - Initial Award: \$ 2,026,422.00

Prepared by: Vincent Baglivo, PE  
Project Manager  
Colliers Engineering & Design

James Winckowski, PE, County Engineer
