

Construction Management and Inspection Services



CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22
Federal Project No. STBGP-PHILA-0613(301)
NJDOT Job No. 5809322
ERI Job #:30750 71
Township of Cherry Hill
County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #29
December 25, 2023 to January 5, 2024



Figure: 1 – Installation of stop sign and pedestrian crossing sign at the intersection with Millstream Drive



Figure: 2 – Installation of pedestrian crossing sign at the entrance to the Cherry Valley Swim Club

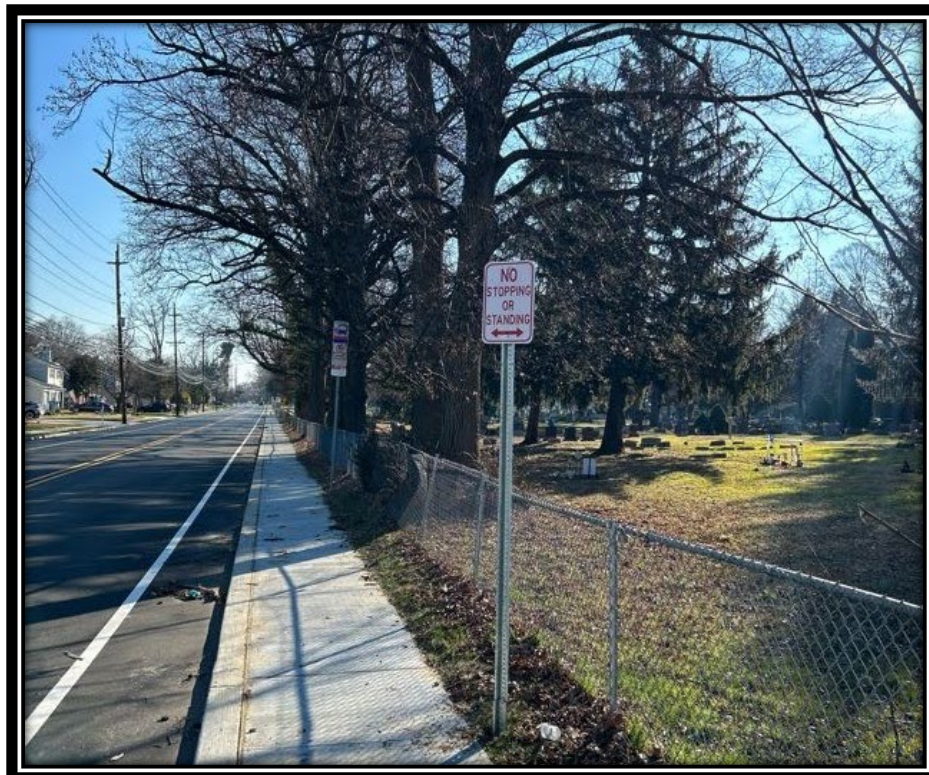


Figure: 3 – Installation of no stopping or standing signs along the eastbound lane between Millstream Drive and King's Highway

Work Completed the Weeks of December 25, 2023 & January 1, 2024:

Black Rock's signage subcontractor, Straight Edge, mobilized to the site to install all regulatory and warning signage for the entire project. Straight Edge installed 620 square feet of regulatory and warning signs.

#60: Regulatory and Warning Signs – 620 SF

Anticipated Work for the Weeks of January 8, 2024 & January 15, 2024:

The project is now substantially complete. Black Rock will return in the spring to complete the seeding and punch list work.

Bid Opening Date: March 31, 2022

Amended Notice to Proceed Date: March 27, 2023

Start Date: March 27, 2023

Substantial Completion Date: December 29, 2023

Anticipated Final Completion Date: March 31, 2024

Amended Contract Completion Date: March 31, 2024

Contract Completion Percentage: 95.23%

Initial Project Cost: \$4,200,000.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
