

Construction Management and Inspection Services



CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22
Federal Project No. STBGP-PHILA-0613(301)
NJDOT Job No. 5809322
ERI Job #:30750 71
Township of Cherry Hill
County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #23
October 2, 2023 to October 13, 2023

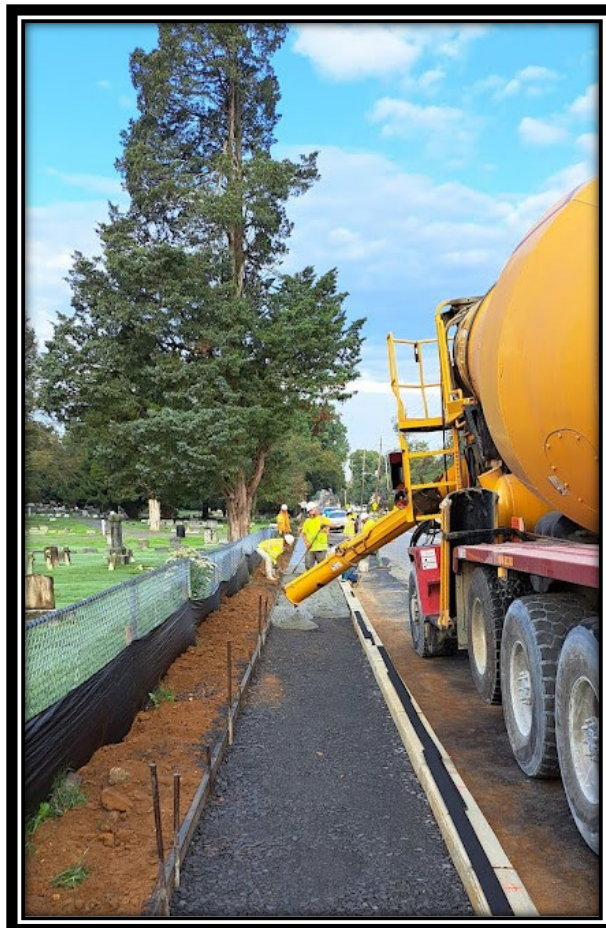


Figure: 1 – Installation of concrete sidewalk along the eastbound lane between Millstream Drive and King’s Highway



Figure: 2 – Installation of 16" DIP at the intersection with Washington Avenue



Figure: 3 – Installation of Type ' B ' inlet at the intersection with Oak Avenue

Work Completed the Weeks of October 2, 2023 & October 9, 2023:

Black Rock's concrete subcontractor, Discover Construction, completed concrete improvements along the eastbound and westbound lanes between Wilson Road and Lake Drive West. Discover also installed the additional sidewalk along the eastbound lane between Millstream Drive and King's Highway. Discover installed 953.45 square yards of concrete sidewalk, 1,236 linear feet of concrete vertical curb, 24.57 square yards of 6" thick, reinforced concrete driveway apron and 16.82 square yards of detectable warning surface. Black Rock's pipe crew continued drainage improvements between Lake Drive East and Oak Avenue. Black Rock installed 2 type B inlets, 29 linear feet of 12" DIP, 18 linear feet of 16" DIP and 423 linear feet of 18" RCP. Black Rock's restoration crew also installed 371.2 square yards of topsoil, seeding and fertilizer.

#5: Police-Uniform Law Enforcement Officer – 156 MH

#21: 12" DIP – 29 LF

#23: 16" DIP – 18 LF

#26: 18" RCP – 423 LF

#40: Concrete Sidewalk, 4" Thick – 953.45 SY

#42: Concrete Driveway, Reinforced, 6" Thick – 24.57 SY

#43: Detectable Warning Surface – 16.82 SY

#44: 9" x 16" Concrete Vertical Curb – 1,236 LF

#68: Topsoiling, 4" Thick – 371.2 SY

#69: Fertilizing & Seeding, Type F – 371.2 SY

#S6: Type 'B' Inlet, 6' to 8.5' Deep – 2 Units

Anticipated Work for the Weeks of October 16, 2023 & October 23, 2023:

Discover Construction has caught up to Black Rock's drainage crew and will leave the site for approximately 2 weeks. Black Rock will continue drainage improvements between Lake Drive East and Oak Avenue. Black Rock's restoration crew will continue curb trench and topsoil & seeding restoration throughout the project limits.

Bid Opening Date: March 31, 2022

Amended Notice to Proceed Date: March 27, 2023

Start Date: March 27, 2023

Anticipated Completion Date: December 1, 2023

Contract Completion Date: December 31, 2023

Contract Completion Percentage: 47.18%

Initial Project Cost: \$4,200,000.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
