



Making It Better, Together.

## Bid Number B1-23

### Maintenance of Thermoplastic Painting on CR 700 Series Roads

#### Various Municipalities, Camden County, New Jersey

### Progress Report #1

### Week Ending April 19, 2024

#### Project Overview:


The project has been awarded to Zone Striping, Inc. in the amount of \$385,333.<sup>77</sup>. The Notice to Proceed was issued with a start date of Monday, April 1, 2024. The estimated construction duration is **seventy (70) calendar days for Substantial Completion** and **one hundred (100) calendar days for Final Completion**. The date for Substantial Completion is **Tuesday, June 10, 2024** and the date of Final Completion is **Thursday, July 10, 2024**.

The work to be performed under this contract shall consist of the Maintenance of Thermoplastic Markings (Cross Walks, Stop Bars, Arrows, Railroad Crossing, Shark's Teeth and Bike Symbols), Letters and Gore Striping on County Route 700 Series roads in the various municipalities of Camden County. Four different types of cross walks are utilized in Camden County consisting of Continental, Ladder, Standard and Zebra. These will be replaced in-kind.

The limits of thermoplastic maintenance at intersections are defined as follows:

<u>Intersection Type</u>	<u>Limits</u>
CR700/CR700	All thermoplastic gets replaced.
CR700/Non-700 Series County Route	700 Series Road gets all thermoplastic replaced and non-700 series road gets the cross walk and stop bar replaced. No approaching gore striping or lane arrows get replaced on the non-700 series county road.
CR700/Municipal Road	Municipal road cross walks and stop bars, if present, will be getting replaced under this contract.
CR700/NJSH Road	Only the 700 series road gets thermoplastic replaced. No thermoplastic work is proposed on state highways.


## Location Map - 700 Series County Roads, northern Camden County

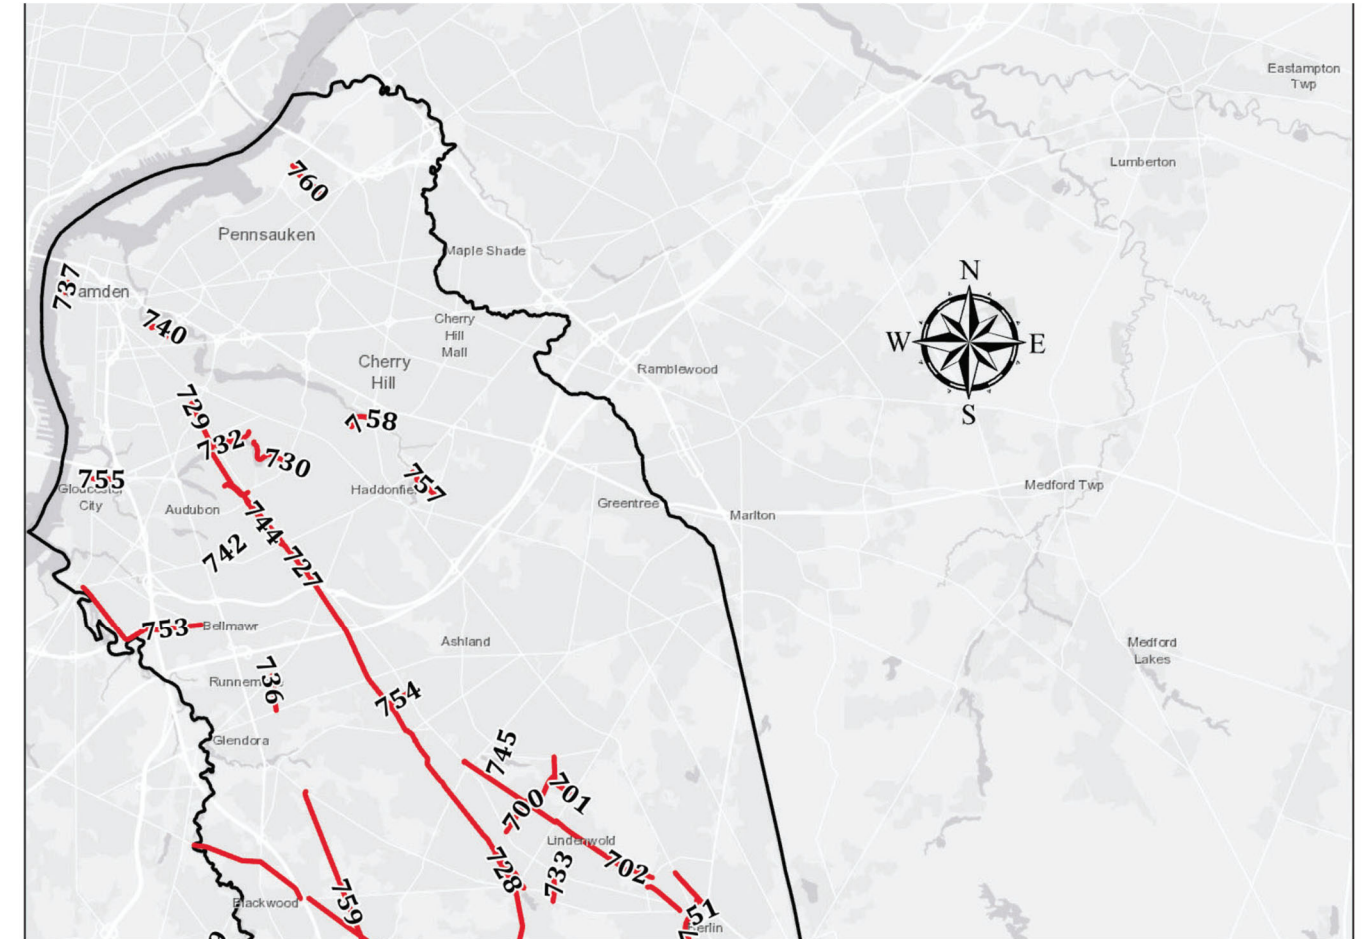

Match Line (see next page)

## Location Map - 700 Series County Roads, southern Camden County

Match Line (see previous page)

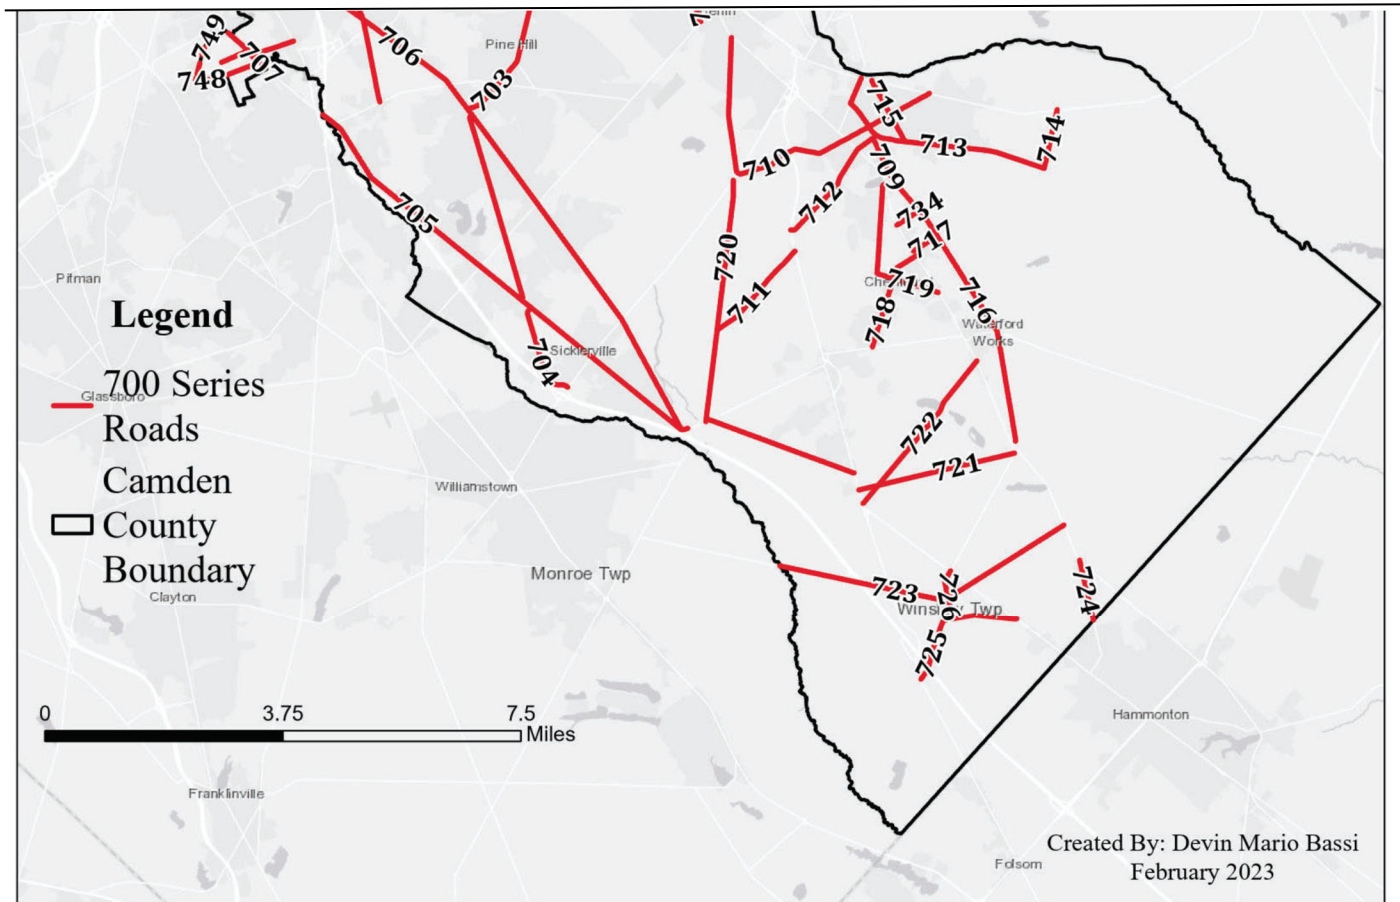

Department of  
Public Works

Almar Dyer  
Commissioner, Liaison

Robert Harris  
Director



Making It Better, Together.

Department of Public Works  
Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)  
[CamdenCounty.com](http://CamdenCounty.com)

### Progress Photographs:



Photograph 1 – 24" White Thermoplastic Stop Bar being installed by Zone Striping on Vineyard Road (CR 719) at the intersection with the White Horse Pike in Waterford Township.



Photograph 2 – Typical Standard Crosswalk being installed at the Atco Avenue (CR 710) intersection with Carl Hasselman Drive.



Photograph 3 – Typical Railroad Crossing symbols being installed on Atco Avenue (CR 710).



Photograph 4 – Typical “ONLY” and Lane Turn Arrows being installed on Atco Avenue (CR 710 near the White Horse Pike.



Photograph 5 – Typical Yellow Gore Striping installed on Cooper Road (CR 713).

### Work Completed this Report Cycle:

- The start of construction was delayed by one week due to the weather forecast of rain during the week of April 1, 2024. Construction actually started on Monday, April 8, 2024 with thermoplastic being installed for Stop Bars, Cross Walks, Railroad Crossings and Rumble Strips on CR 721, CR 716, CR 709 and CR 722. Work continued throughout the southern portion of Camden County during this reporting cycle.

### Changes to the Initial Contract items:

- Work Directive #1 for the Rumble Strips encountered on CR 723 was approved by the County Engineer at a rate of \$4.20 per linear foot. (see attached signed Work Directive). The Supplemental Item for Rumble Strips will be incorporated into the contract in a future Change Order.

### Project Schedule:

- Bid Opening Date: September 13, 2023
  - Notice to Proceed: April 1, 2024
  - Start Date: April 8, 2024
  - Initial Completion Date: July 10, 2024
  - Stop Work: N/A
  - Amended NTP: N/A
  - Final Completion Date: Unchanged, July 10, 2024
  - Initial Award: \$385,333.77
  - Contract Value: \$385,333.77
- 
- Status of Work Completed to Date based on approximate percentages:
    - Overall Project: 19% ±
    - Time Used to Date: 19.0%
    - Paid to Date: 0.00% No Payment Applications to date.

Prepared by: Mark R. Basehore, Jr., PE, CME  
Bach Associates, PC

# PROPOSAL



718 Jacob Harris Lane  
P.O. Box 568  
Glassboro, NJ 08028  
Ph. 856-582-5900  
Fax 856-582-1303

DATE: April 9, 2024  
TO: Camden County  
520 Market Street  
Camden, NJ 08102

ATTN: Vibhuti Bhimani  
PHONE: 856-566-2938  
FAX:  
EMAIL:

[Vibhuti.Bhimani@camdencounty.com](mailto:Vibhuti.Bhimani@camdencounty.com)

**ZONE JOB # N23-694**

**Bid #B1-23 Maintenance Roadway Painting on  
700 Series Thermoplastic Line Striping  
Various Municipalities, Camden County**

<u>ITEM NO.</u>	<u>QUANTITY</u>	<u>UNIT</u>	<u>DESCRIPTION</u>	<u>PRICE</u>	<u>UNIT</u>	<u>AMOUNT</u>
X-1	-	LF	8" Wide Lines - Rumble Strip Striping	4.20	LF	

**NOTES:**

Acceptance Signature \_\_\_\_\_

A handwritten signature in blue ink, appearing to read "Vibhuti", is written over a horizontal line.

A handwritten signature in black ink, appearing to read "Paul R. Mitchell, Jr.", is written over a horizontal line.

PAUL R. MITCHELL, JR./PRESIDENT

PAYMENT TERMS: 5 DAYS AFTER RECEIPT  
OF PAYMENT FROM OWNER  
PRICE FIRM 60 DAYS FROM DATE OF BID
