

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

**Kaighn Avenue Dam – East Tide Gate
(NJDEP Dam #31-066)
*Bid No. B1-24***

*Township of Pennsauken and City of Camden
Camden County, New Jersey*

CED Project No. 230005437G2

Progress Report #9

Monday, August 19, 2024, to Friday, August 30, 2024



*Figure:1
New Crane Rails.*

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

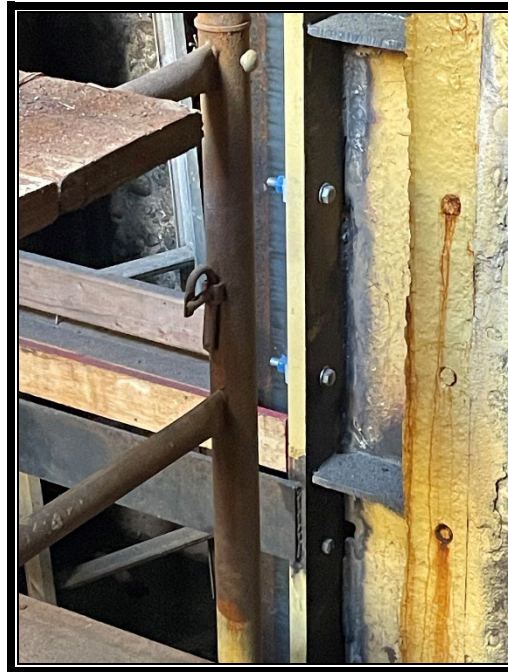


Figure 2: New Crane Rails With Stiffeners.

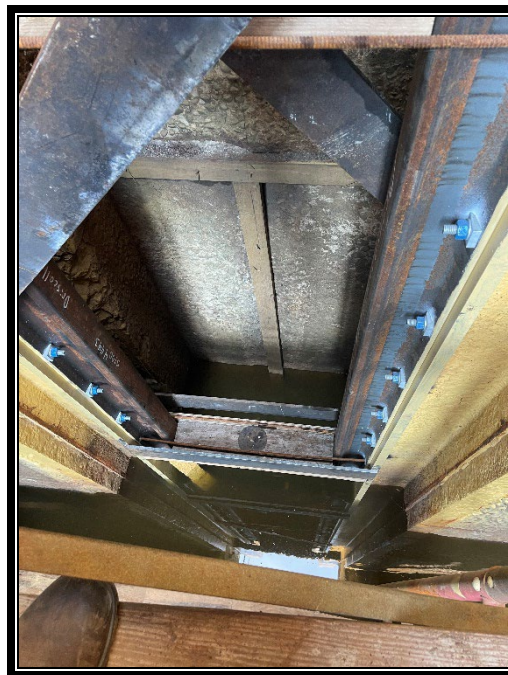


Figure 3: New Crane Rails set East side.

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

- **Work Completed this week:**
 - Contractor continues dewatering
 - Contractor continues working in Cofferdam on structure and rails.
 - Installing new crane rails and supports, welding Flange, and stiffener plates.

- **Progress Next Two Weeks:**
 - Continue tide gate & Structure rehabilitation.

- **Next Progress Meeting:**
 - The next Progress Meeting has been rescheduled for Thursday, September 5, 2024 at 2:30 PM.

- Bid Award Date: March 21, 2024
- Notice to Proceed: April 29, 2024
- Start Date: May 7, 2024
- Substantial Completion Date: October 25, 2024
- Stop Work: N/A
- Amended NTP: N/A
- Final Completion Date: November 14, 2024
- Initial Award: \$ 2,026,422.00

Prepared by: Sean Hoolahan
Resident Engineer
Colliers Engineering & Design

James Winckowski, PE, County Engineer
