

Construction Management and Inspection Services



CHURCH ROAD (CR 616) ROADWAY IMPROVEMENTS, B3-22
Federal Project No. STBGP-PHILA-0613(301)
NJDOT Job No. 5809322
ERI Job #:30750 71
Township of Cherry Hill
County of Camden, New Jersey

WEEKLY PROGRESS REPORT #18
August 14, 2023 to August 18, 2023



Figure: 1 – Installation of reinforced concrete driveway apron, sidewalk and curb along the westbound lane between King's Highway and Friendship Drive



Figure: 2 – Topsoil, seed and fertilizer restoration around newly installed ADA ramp and concrete sidewalk along the westbound lane at the intersection with Crofton Commons

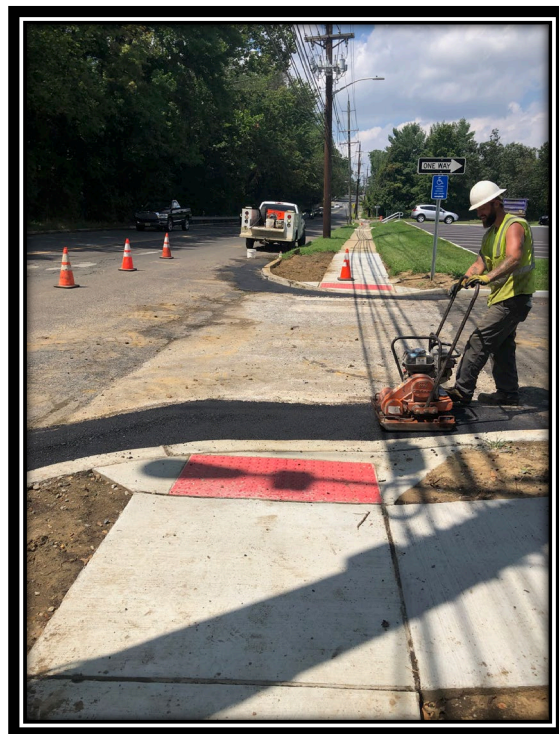


Figure: 3 – HMA restoration around newly installed ADA ramp and curb along the westbound lane in front of the Thomas Paine Elementary School

Work Completed the Week of August 14, 2023:

Black Rock's concrete subcontractor, Discover Construction, continued the concrete improvements along both the westbound and eastbound lanes between King's Highway and Millstream Drive. Discover installed 82 square yards of concrete sidewalk, 1,703 linear feet of concrete vertical curb and 42.7 square yards of 6' thick, reinforced concrete driveway apron. Black Rock's pipe crew completed the installation of drainage improvements between Roosevelt Drive and Cleveland Avenue and then began HMA curb trench and topsoil, seed & fertilizer restoration on the east side of the project. The pipe crew installed 128.5 linear feet of 12" DIP, reconstructed 1 inlet and 295.6 square yards of topsoil, seed & fertilizer.

- #5: Police-Uniform Law Enforcement Officer – 131.5 MH**
- #21: 12" Ductile Iron Pipe, Class 53 – 128.5 LF**
- #35: Reconstruct Inlet Type E, Using New Casting – 1 Unit**
- #40: Concrete Sidewalk, 4" Thick – 47.1 SY**
- #42: Concrete Driveway, Reinforced, 6" Thick – 42.7 SY**
- #44: 9" x 16" Concrete Vertical Curb – 1,703 LF**
- #68: Topsoiling, 4" Thick – 265.6 SY**
- #69: Fertilizing & Seeding, Type F – 265.6 SY**
- #CH1: Concrete Sidewalk, 4" Thick (Cherry Hill) – 34.9 SY**
- #CH7: Topsoiling, 4" Thick (Cherry Hill) – 30 SY**
- #CH8: Fertilizing & Seeding, Type F (Cherry Hill) – 30 SY**

Anticipated Work for the Week of August 21, 2023:

Discover Construction will continue concrete improvements along both the eastbound and westbound lanes between King's Highway and Millstream Drive. Black Rock will complete the HMA curb trench restoration and topsoil and seeding along both lanes between the County line and King's Highway.

Bid Opening Date: March 31, 2022

Amended Notice to Proceed Date: March 27, 2023

Start Date: March 27, 2023

Anticipated Completion Date: December 1, 2023

Contract Completion Date: December 31, 2023

Contract Completion Percentage: 31.73%

Initial Project Cost: \$4,200,000.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
