

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

**Improvements to Kings Highway (C.R. 551-S) from Market Street
(C.R. 634, MP 1.23) to Hopkins Road (C.R. 647, MP 3.65)
*Bid No. B6-24***

*Boroughs of Mount Ephraim, Audubon, and Haddon Heights
Camden County, New Jersey*

CED Project No. 24001861G

Progress Report #4

Monday, October 21, 2024, to Friday, November 1, 2024

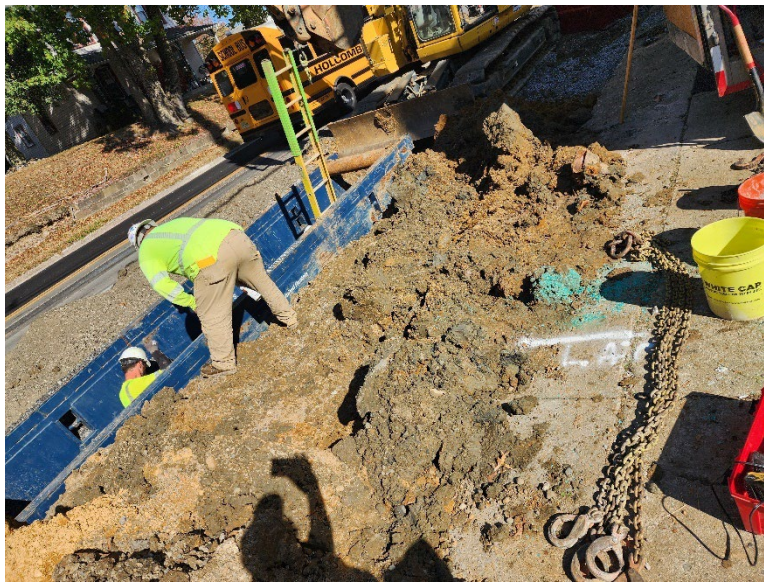


Figure:1

Continued sewer main replacement on eastbound lane & shoulder of Kings Highway.

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Making It Better, Together.

Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com



*Figure 2:
Continued replacement of manhole castings and covers at various locations.*



*Figure 3:
Began replacement of sewer laterals along the EB lane.*



*Figure 4:
Installation of new drainage inlet near the intersection of Market and Kings Hwy.*

- **Work Completed this week:**
 - Removal of previously rubblized pavement
 - Installation of new curbs, sidewalk, and Driveways at selected locations
 - Sewer main and lateral replacement
 - Replacement and resetting of Inlet and manholes.
 - Installation of new drainage inlets
 - Full depth concrete repairs at various locations

- **Items completed this period:**
 - Full depth Concrete repairs
 - Replacement of 15" RCP
 - Reconstruction of inlet
 - Drainage grate replacement
 - Curb piece replacement
 - Inlet filter installation
 - Dense graded aggregate placement
 - Concrete sidewalk 4"
 - Concrete driveway 6"
 - 9" X 18" concrete curb

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

- Removal of concrete pavement
- Inlet type B installation
- Sewer lateral replacement

- **Progress Next Two Weeks:**
 - Curb, sidewalk, and driveway replacement
 - Manhole and inlet reconstruction/reset
 - Sewer main and lateral replacement
 - Full depth concrete repairs
 - Saint rose roof drain reconfiguration
 - Milling and paving segment 2 (Blackhorse to hillside)

- **Next Progress Meeting:**
 - The next Progress Meeting has been scheduled for Tuesday, October 29, 2024, at 9 AM.
 - Bid Award Date: July 18, 2024
 - Notice to Proceed: 9/9/24
 - Start Date: 9/9/24
 - Substantial Completion Date: 340 days, August 15, 2025
 - Stop Work: N/A
 - Amended NTP: N/A+
 - Final Completion Date: September 24, 2025
 - Initial Award: \$10,745,085.83

Prepared by: Obed Okeyo
Resident Engineer
Colliers Engineering & Design

James Winckowski, PE, County Engineer
